

RAILWEAVE

THE CENTENNIAL JINGZHANG AS A CIVIC INNOVATION AXIS

REGIONAL CHAIN | CORRIDOR WEAVE | PLACE-BASED PROJECTS

One axis, three corridors and three hubs form a chain from open problems to validation, first use and knowledge return; ordinary service remains.

CITY FIRST | ORDINARY SERVICE CONTINUES
FIELD WORK REQUIRES CONFIRMED SITE, RIGHTS, DUTIES, AND SPECIALIST CONDITIONS

THREE PLACE-BASED PROJECTS

- 01

ZHONGZHIYUAN | OBSERVABLE VALIDATION YARD

public route—safety buffer—controlled test—human takeover
- 02

AI ORIGIN | OPEN REPAIR STREET

shared arcade—issue clinic—open tools—controlled back room
- 03

DAZHONGSI | FIRST-USE SERVICE CONCOURSE


surface arrival—needs service—human review—quiet waiting

TURN THE INNOVATION CHAIN INTO ONE STREET, ONE SCENARIO, ONE SIGNABLE PILOT.

P01 / L4 + L5 SPATIAL WORKING PLAN

Jing-Zhang AI Innovation Belt Working Plan: Context, Provisional Extent and Action Interfaces

A date-locked open basemap checks spatial relationships while provisional geometry carries design tasks; the layers remain separate and do not replace statutory planning or engineering survey.

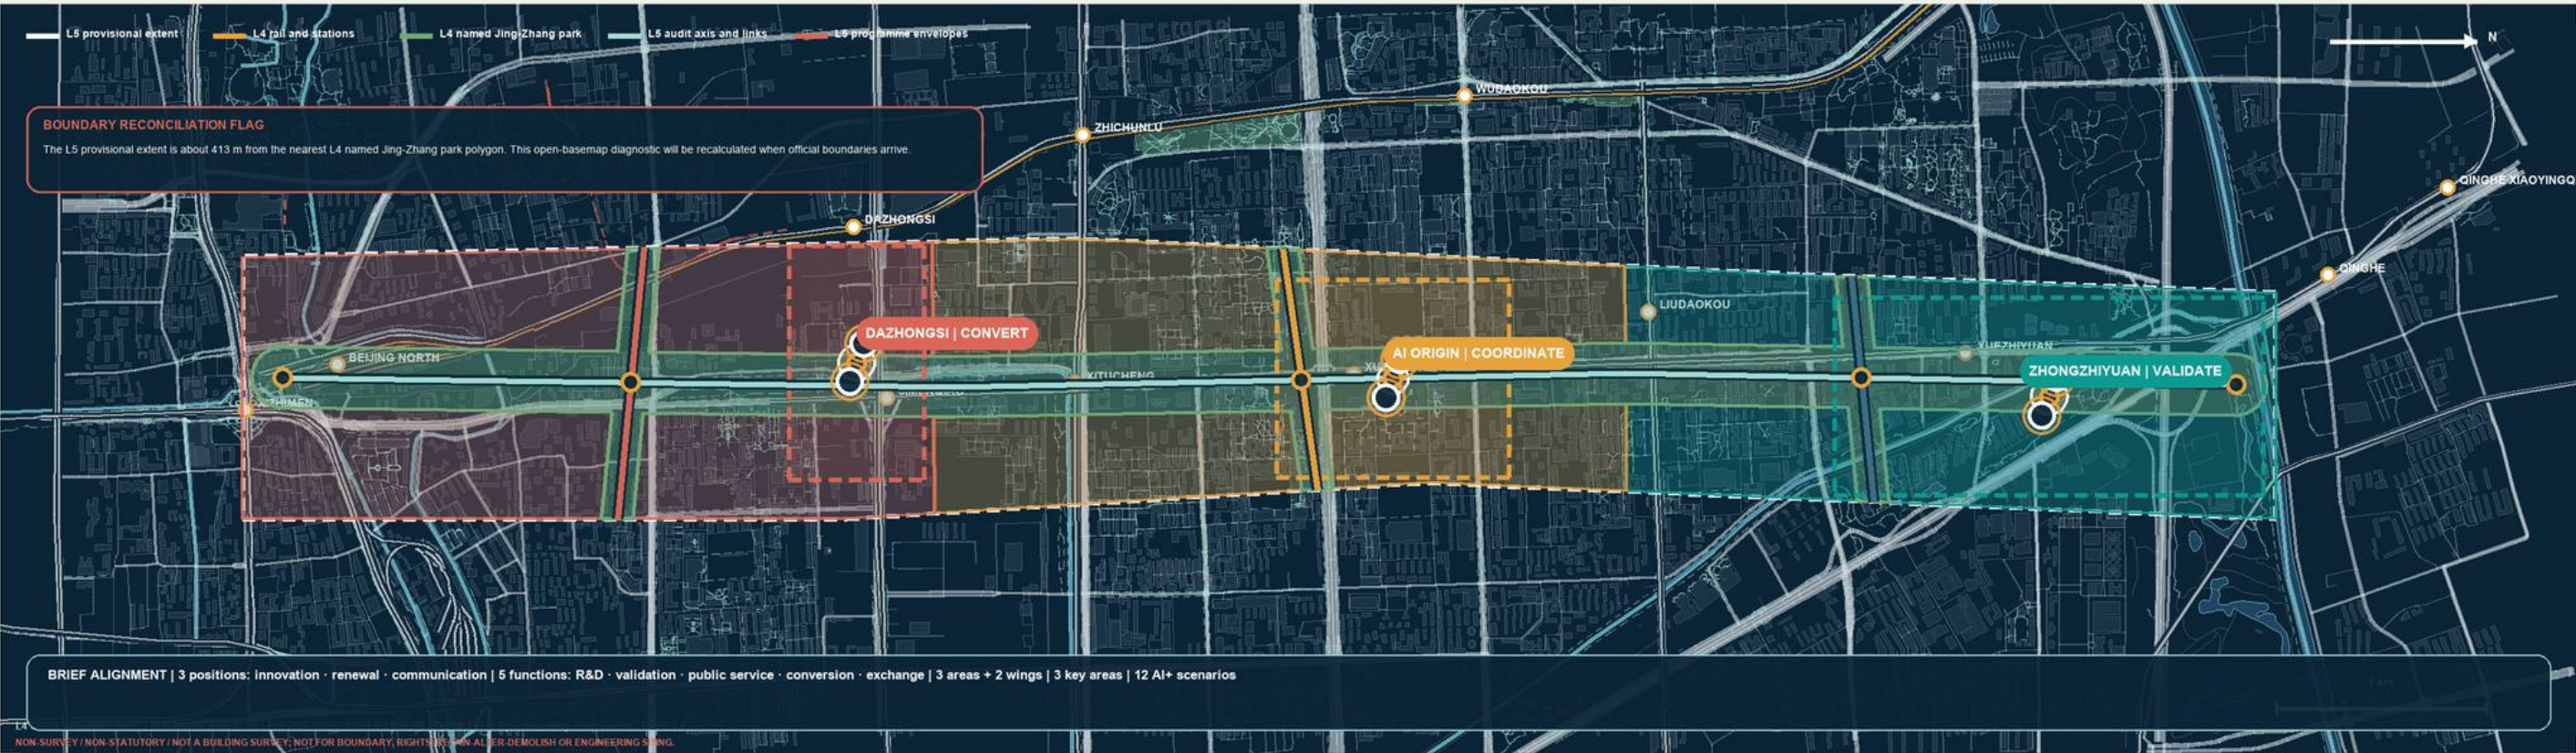

01 NORTH | ZHONGZHIYUAN VALIDATION

Qinghe interface with separated public observation and controlled testing; site only after rights, fire, insurance and independent review.

L4 CONTEXT LEAD + L5 ACTION | SITE AFTER FIELD AND LAWFUL REVIEW

02 CENTRE | AI ORIGIN COORDINATION

Use a verified shared ground floor to connect universities, communities, campuses and talent services while retaining paper, phone and staffed channels.

L4 CONTEXT LEAD + L5 ACTION | SITE AFTER FIELD AND LAWFUL REVIEW

03 SOUTH | DAZHONGSI FIRST USE

Re-anchor the study window to the brief's named station clue; study surface access, demand compliance and removable first-step components only.

L4 CONTEXT LEAD + L5 ACTION | SITE AFTER FIELD AND LAWFUL REVIEW

P04 / THREE PLACE-BASED PLAN-SECTION-OPERATION PROTOTYPES

Three Key Areas: Context Plan, Spatial Experience, Delivery Interface and Responsibility Acceptance

Each area uses an L4 open basemap for real urban context and L5 provisional geometry for design tasks; concept images are not evidence of baseline, buildings, engineering or investment.

01ZHONGZHIYUANCONTROLLED VALIDATION

L4 CONTEXT + L5 STUDY PLAN

8 ENTRY / P1 PRIMARY / P2 SECONDARY / S1 SERVICE/EMERGENCY / Z1-Z4 ZONES / V1 VIEW



L4 OPEN WORKING BASE | BUILDINGS 2026-07-08 | POI 2026-05-06 | OTHER LAYERS 2026-05-11 | © OpenStreetMap contributors / ODbL 1.0
NON-SURVEY / NON-STATUTORY / NOT A BUILDING SURVEY; NOT FOR BOUNDARY, RIGHTS, RETAIN-ALTER-DEMOLISH OR ENGINEERING SITING.

AI CONCEPT / NOT BASELINE



1 Qinghe-Jing-Zhang interface | separate observation and testing

2 AN-V21-007 + ZY-AA/BB | opening, access, isolation and emergency pending

3 DC/PC-ZY-001/002 | removable and restorable; stop if rights/fire/insurance remain open

RESPONSIBILITY AND ACCEPTANCE

Lawfully appoint IE, IV and DC and obtain written receipt; validation remains separate from operations.

ROLE ARCHETYPE → LAWFUL APPOINTMENT → WRITTEN RECEIPT

DIMENSIONS, RIGHTS, ENTRANCES, CONTROL LINES, BUILDINGS AND ENGINEERING ALL REQUIRE FORMAL REVIEW

02AI ORIGINDEMAND COORDINATION

L4 CONTEXT + L5 STUDY PLAN

8 ENTRY / P1 PRIMARY / P2 SECONDARY / S1 SERVICE/EMERGENCY / Z1-Z4 ZONES / V1 VIEW



L4 OPEN WORKING BASE | BUILDINGS 2026-07-08 | POI 2026-05-06 | OTHER LAYERS 2026-05-11 | © OpenStreetMap contributors / ODbL 1.0
NON-SURVEY / NON-STATUTORY / NOT A BUILDING SURVEY; NOT FOR BOUNDARY, RIGHTS, RETAIN-ALTER-DEMOLISH OR ENGINEERING SITING.

AI CONCEPT / NOT BASELINE



1 University-community-campus network | shared ground floor retains staffed ordinary service

2 AN-V21-005 + AI-AA/BB | floor, rights, fire and hours pending

3 DC/PC-AI-001/002 | movable and pausable; paper/phone/staff remain available

RESPONSIBILITY AND ACCEPTANCE

Lawfully appoint IE, DO and PO and obtain written receipt; refusing AI adds no charge, unreasonable wait or off-site trip.

ROLE ARCHETYPE → LAWFUL APPOINTMENT → WRITTEN RECEIPT

DIMENSIONS, RIGHTS, ENTRANCES, CONTROL LINES, BUILDINGS AND ENGINEERING ALL REQUIRE FORMAL REVIEW

03DAZHONGSIFIRST-USE CONVERSION

L4 CONTEXT + L5 STUDY PLAN

8 ENTRY / P1 PRIMARY / P2 SECONDARY / S1 SERVICE/EMERGENCY / Z1-Z4 ZONES / V1 VIEW



L4 OPEN WORKING BASE | BUILDINGS 2026-07-08 | POI 2026-05-06 | OTHER LAYERS 2026-05-11 | © OpenStreetMap contributors / ODbL 1.0
NON-SURVEY / NON-STATUTORY / NOT A BUILDING SURVEY; NOT FOR BOUNDARY, RIGHTS, RETAIN-ALTER-DEMOLISH OR ENGINEERING SITING.

AI CONCEPT / NOT BASELINE



1 Dazhongsi surface station edge-demand compliance interface | no assumed underpass

2 AN-V21-003 + DZS-AA/BB | re-anchored to named station clue; entrances and peak flow pending

3 DC/PC-DZS-001/002 | day-90/180 review; stop if demand/budget/procurement/exit remain open

RESPONSIBILITY AND ACCEPTANCE

Lawfully appoint DO, PF and IE and obtain written receipt; renew, correct or exit with receipts.

ROLE ARCHETYPE → LAWFUL APPOINTMENT → WRITTEN RECEIPT

DIMENSIONS, RIGHTS, ENTRANCES, CONTROL LINES, BUILDINGS AND ENGINEERING ALL REQUIRE FORMAL REVIEW

P01 / DELIVERY LEDGER

Project Gates, Responsibility and Five-Year Operating Account

A project does not advance while site, demand, data, funding, procurement, acceptance, operations or exit responsibility remains unresolved.



RW-A01

AI Origin Demand Room

Input

problem evidence pack

Acceptance artifact

demand brief + response

Stop condition

unclear demand / rights

RW-B01

Zhongzhiyuan Validation Lab

Input

version + test brief

Acceptance artifact

reproducible pack + review

Stop condition

major risk unresolved

RW-C01

Dazhongsi First-Use Operations Pool

Input

demand + validation + WLC cost

Acceptance artifact

launch list + post-review

Stop condition

procurement / OPEX unaffordable

S06 | 100-DAY BOUNDED DELIVERY: FOUR PHASES, SIX DECISION WINDOWS

P1 | DAYS 0-30

SITE + BASELINE

Days 0-10 site checks; Days 11-30 route, ordinary-service and staff baseline

stop if rights, access, or ordinary service remains open

P2 | DAYS 31-60

COST + CLOSED TEST

Days 31-45 quantities, quotes, duty; Days 46-60 shadow log and restoration drill

return on data, takeover, or restoration failure

P3 | DAYS 61-90

BOUNDED CO-TEST

time-limited co-test after lawful authority; mandatory close-out and exit handoff on Day 90

do not start without authority; pause on a serious event

P4 | DAYS 91-100

RESTORE + DECIDE

revoke, delete, remove, restore signs and staffed service; issue one of four written opinions

no next phase if any of six exit receipts is missing

HANDOFF: role archetype → lawful appointment → written IE/DO/PO/IV receipt as applicable; exit resources are itemised, with no fixed percentage.

FIVE-YEAR COST EVIDENCE TC5

$C0 + \Sigma(Ot + Mt + Pt + Vt + At + Rt) + U + X$

G0

verify quantities and service volumes

PENDING

G1

real demand, non-AI baseline and staff

BASELINE

G4

lawful price search, market research or inquiry

UNPRICED

G4+

budget approval, effective contract or funds received

NOT SECURED

10 evidence categories: premises | equipment | staff | accessibility/ordinary service | validation | participation | insurance/emergency | maintenance | renewal | exit/restoration

Items with unverified quantity, price, responsibility or scope stay outside any firm total.

P03 / ACCESS, RAIL AND BLUE-GREEN AUDIT

Jing-Zhang Public Axis and Three Cross-Links: Nine Segments, Eight Anchors and Six Field Tests

L4 road, walking, cycling, rail, station and water leads are overlaid with L5 audit tasks; coloured lines and points do not establish opening, compliance or engineering alignment.



SIX TESTS PER SEGMENT


- 01 Opening & barriers**
date, hours, detour
- 02 Step-free continuity**
slope, width, steps, lift
- 03 Walk, cycle & crossing**
conflict, wait, help
- 04 Rail & waterside**
protection, control, flood
- 05 Night & emergency**
lighting, patrol, emergency access
- 06 Operations & exit**
duty, restoration, receipt

PRECONDITION FOR VERIFIED METRICS
field record + affected-user review + professional opinion + accountable receipt, every segment remains unverified beforehand.

P02 / PROGRAMME ENVELOPES ON CONTEXT

Programme Envelopes and Reversible Components: Gated Siting in the Existing Urban Fabric

Four programmes express action tasks and six components express candidate indexes only; none changes statutory land use or assumes building decisions, development intensity or build scale.

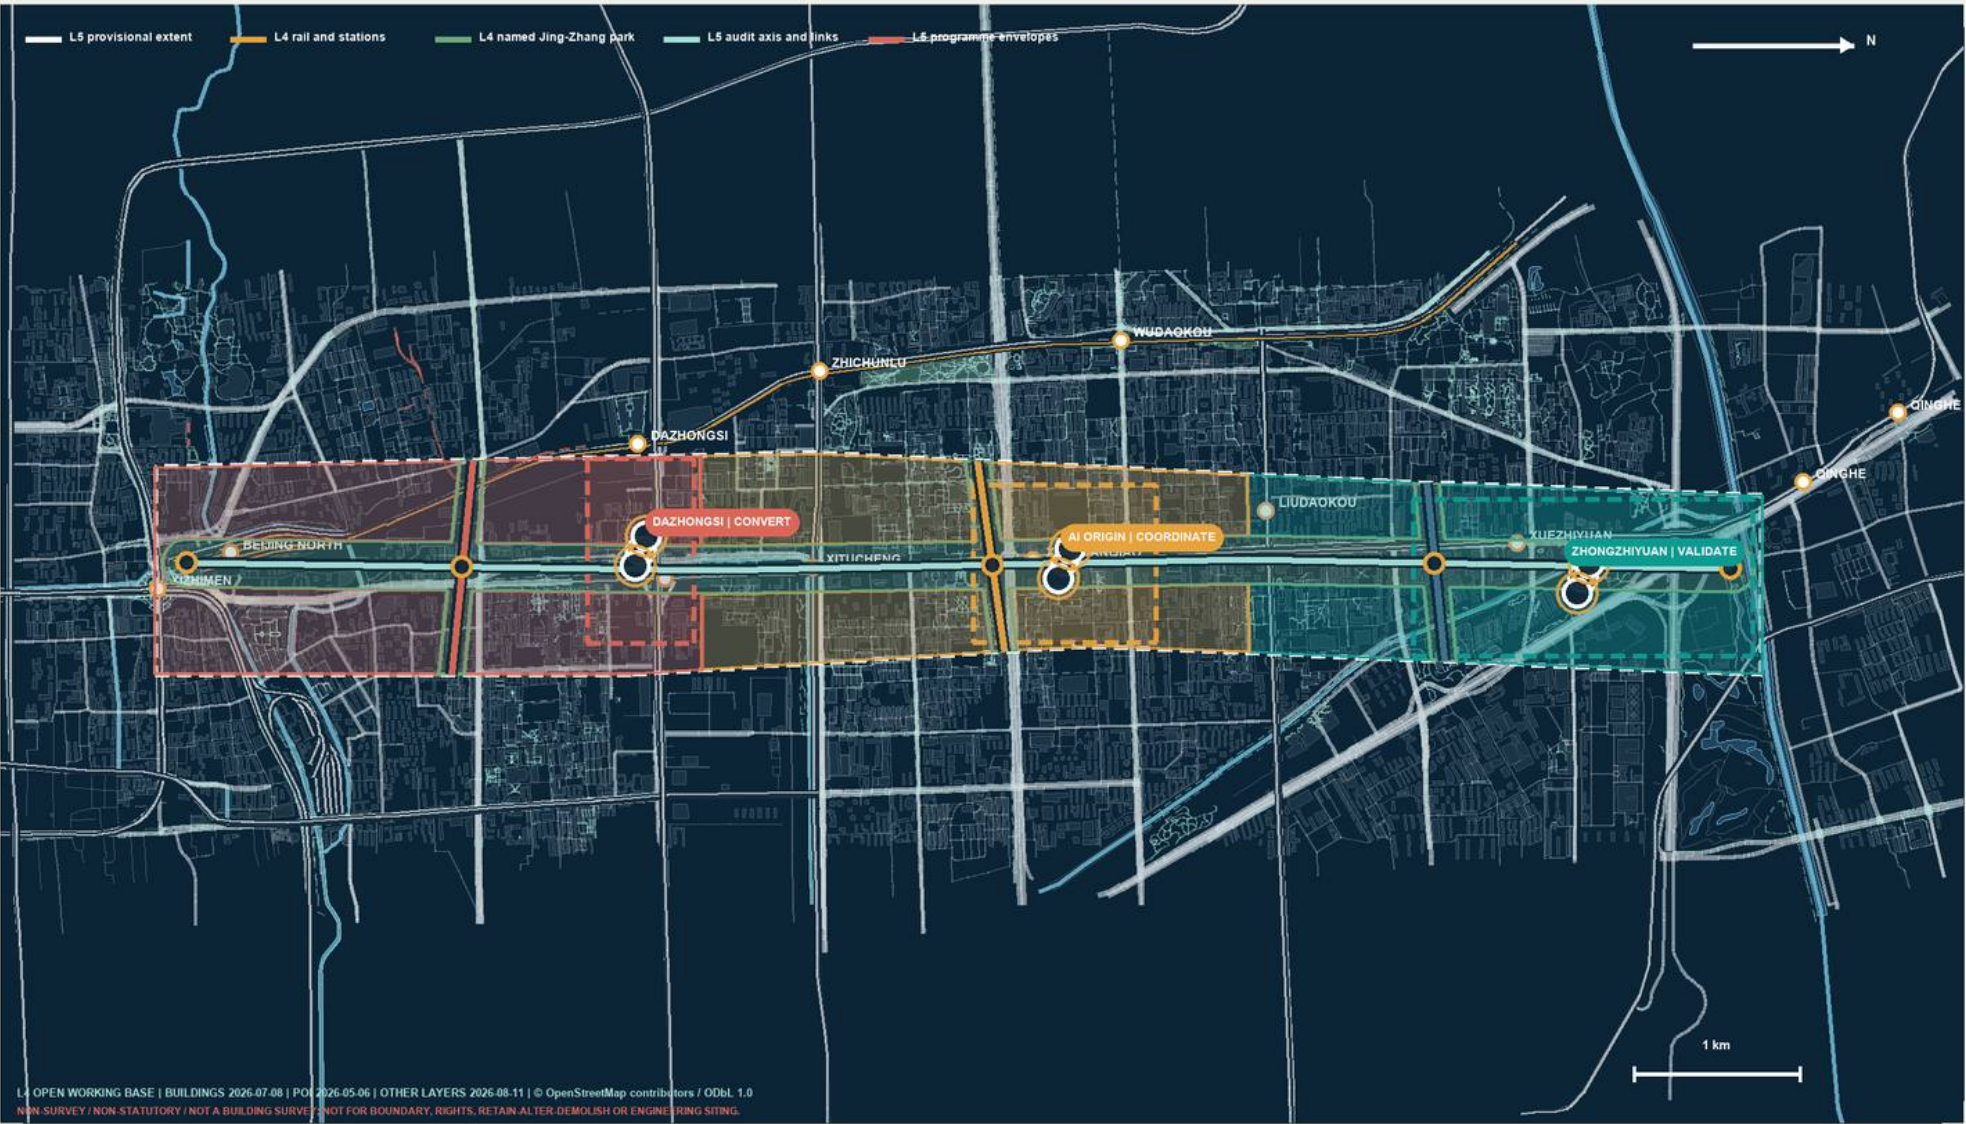

01 Open validation & R&D

Zhongzhiyuan: public observation, controlled testing, independent finding

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

02 Near-campus learning & talent

AI Origin: shared ground floor, ordinary service, distributed coordination

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

03 First-use & composite service

DAZHONGSI: real demand, lawful procurement, review and exit

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

04 Public axis & blue-green links

Nine segments and eight anchors; no continuous-open claim before verification

L5 ACTION ENVELOPE | LAND USE AND RIGHTS PENDING

COMPONENT SITING ORDER


task → study window → component candidate → G0 site/rights → G1 demand/public → G2 controlled prototype

If any statutory or professional condition remains open, keep the component movable, pausable and withdrawable.


D01 / OVERALL URBAN DESIGN WORKING PLAN

One Axis, Three Corridors, Three Hubs: Spatial Structure and Project Loop on One Review Plate

Spatial links, key areas and project gates share one identifier system; mapped relationships are working proposals, not statutory roads, waterways, land use or construction plans.

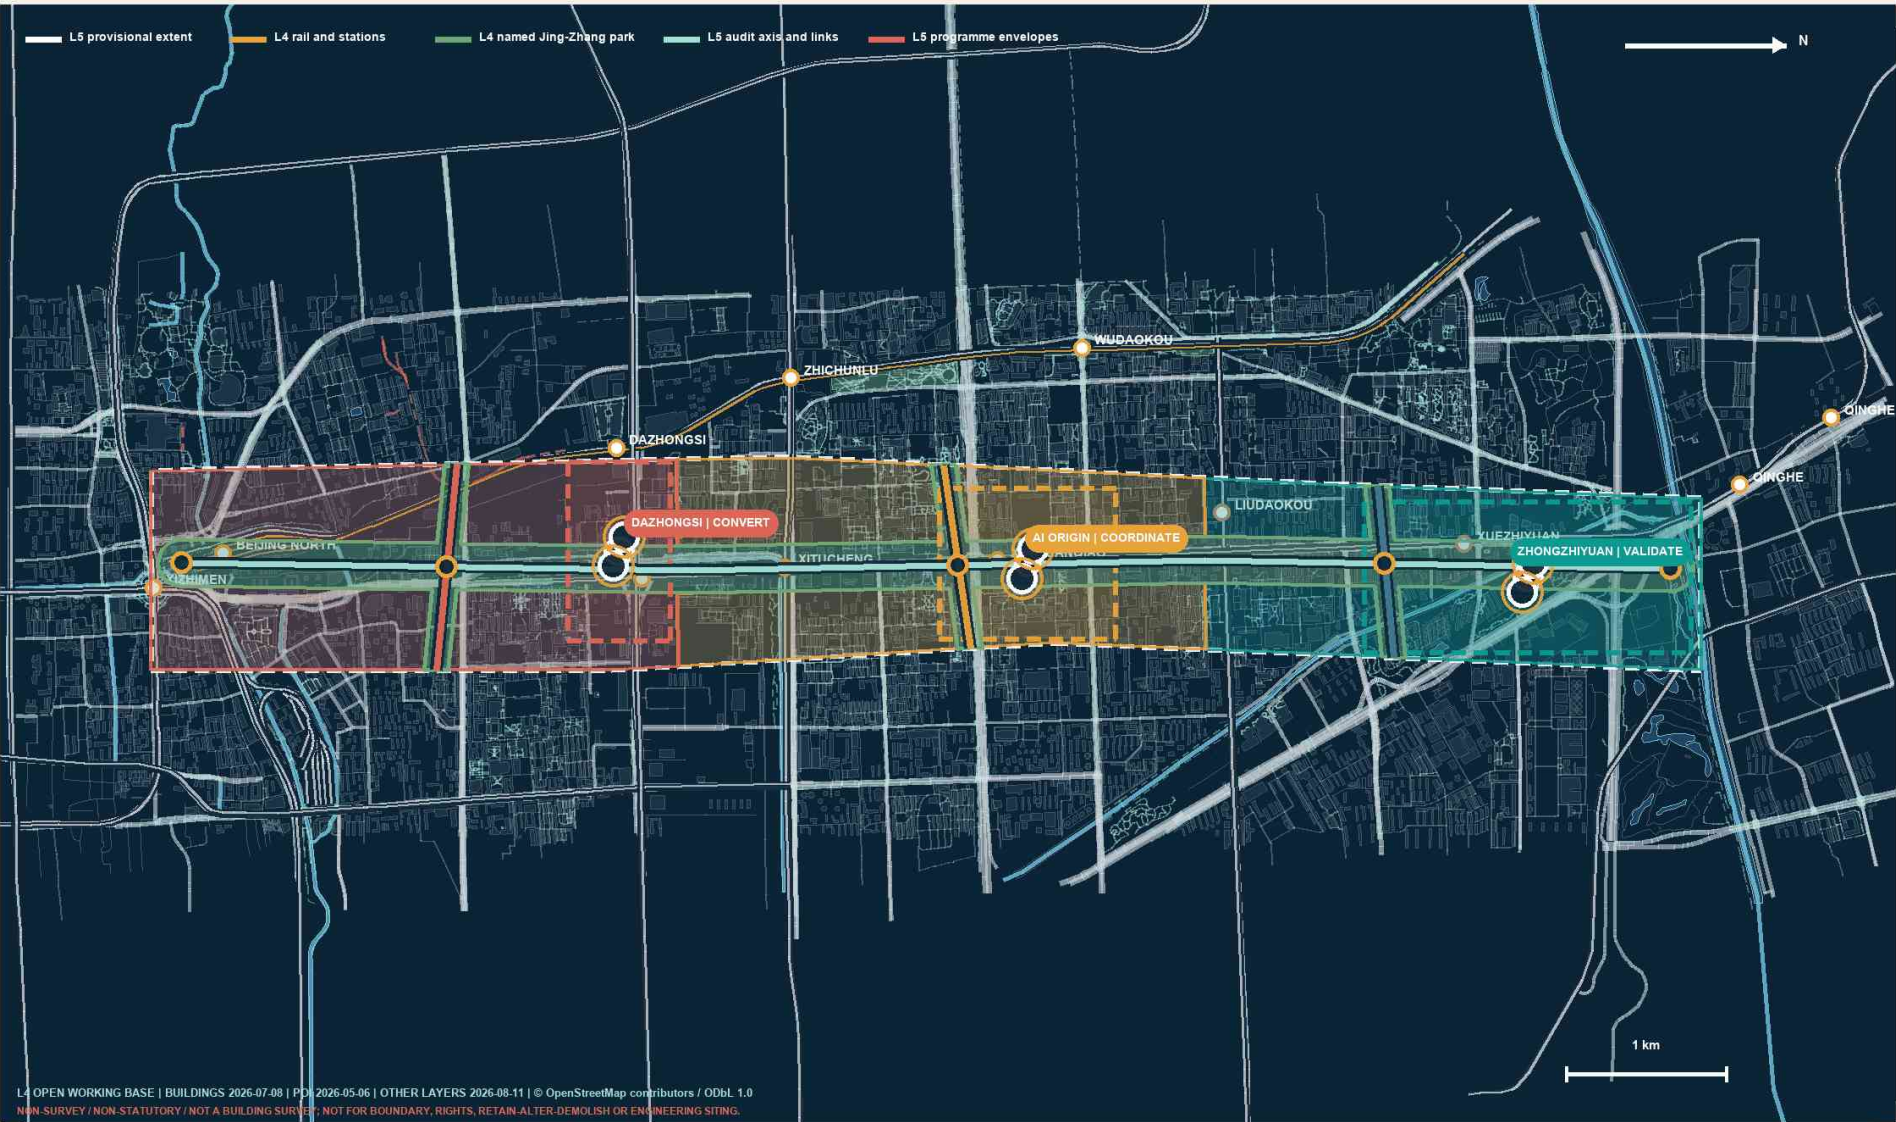

THREE-CHAIN PROJECT LOOP

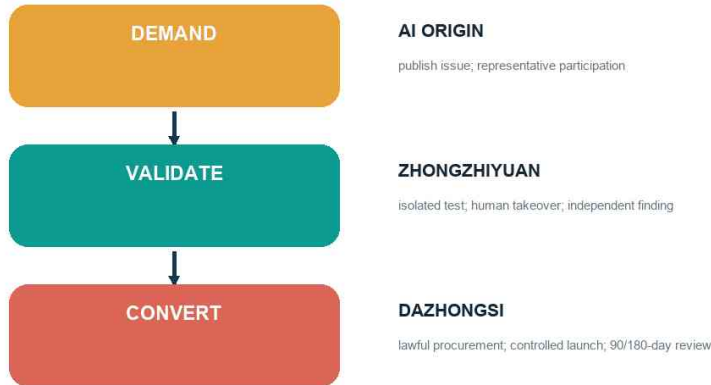

BRIEF ALIGNMENT

3 positions	innovation, renewal, communication
5 functions	R&D, validation, public service, conversion, exchange
3 areas + 2 wings	three differentiated hubs with cross-axis inputs and outputs
3 key areas	L4 context + L5 plan + AA/BB sections + delivery register
AI+ scenarios	12 scenarios, dual gates, human final review and exit restoration

C1 / KEY-AREA PLAN-SECTION-OPERATION



Zhongzhiyuan · Controlled Validation System

Four zones—public observation, semi-controlled validation, controlled testing, and service/emergency—prioritising verified indoor reuse.



MAPPED OBJECTS AND REVIEW INTERFACES

WINDOW	KEY-001
AUDIT	AN-007
SECTION	SEC-ZY-AA / SEC-ZY-BB
COMPONENT	DC-ZY-001 / DC-ZY-002
PLAN ACTIONS	E1/E2/ES + P1/P2/S1 + Z1-Z4 + VIEW

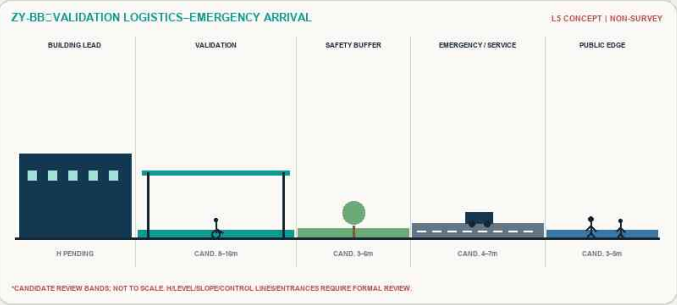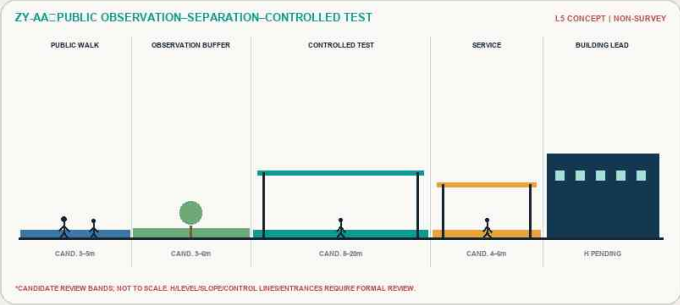

SPACE-OPERATION-EXIT LOOP




G0-G6 retains an audit trail; keep BLOCK if any site, rights, public, risk, cost, procurement or exit condition remains open.

C2 / KEY-AREA PLAN-SECTION-OPERATION


AI Origin · Distributed Demand-Coordination Network

Start with one shared ground floor with verified rights, fire safety and opening hours, linked to communities, universities and talent services.

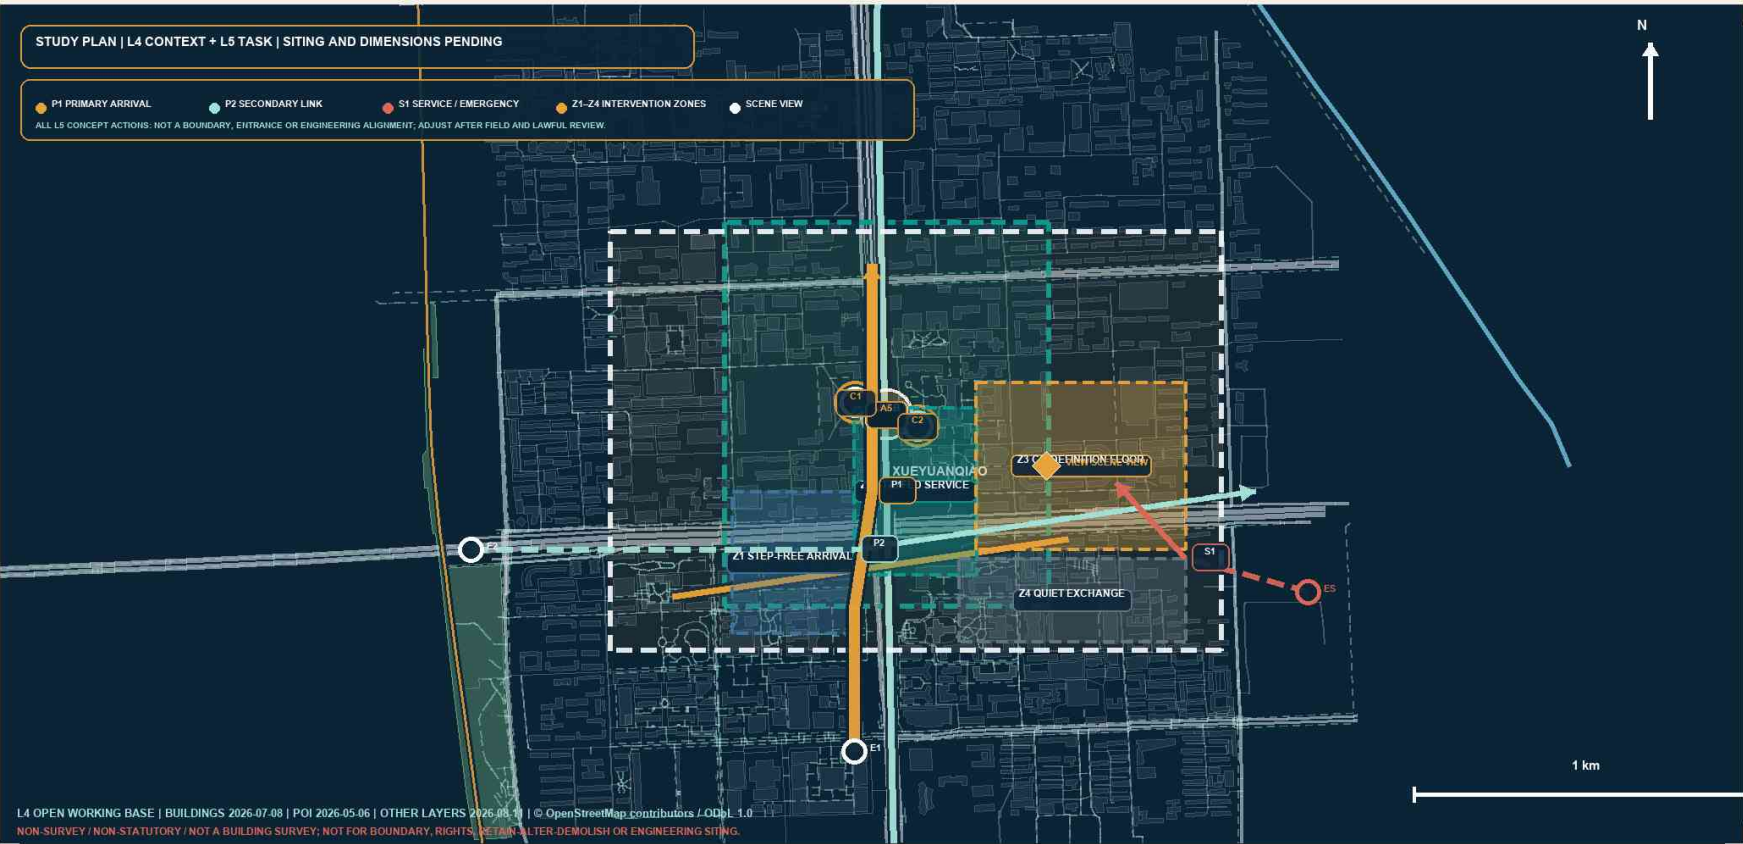

MAPPED OBJECTS AND REVIEW INTERFACES

WINDOW	KEY-002
AUDIT	AN-005
SECTION	SEC-AI-AA / SEC-AI-BB
COMPONENT	DC-AI-001 / DC-AI-002
PLAN ACTIONS	E1/E2/ES + P1/P2/S1 + Z1-Z4 + VIEW

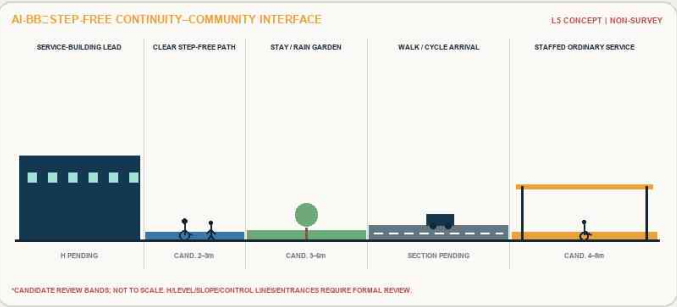

SPACE-OPERATION-EXIT LOOP




G0-G6 retains an audit trail; keep BLOCK if any site, rights, public, risk, cost, procurement or exit condition remains open.

C3 / KEY-AREA PLAN-SECTION-OPERATION



Dazhongsi · Station–City First-Use Interface

Organise surface continuity from the named Dazhongsi station's exterior context to demand service, the Jing-Zhang axis and Zhuan River; no specific entrance or underground connection is assumed.

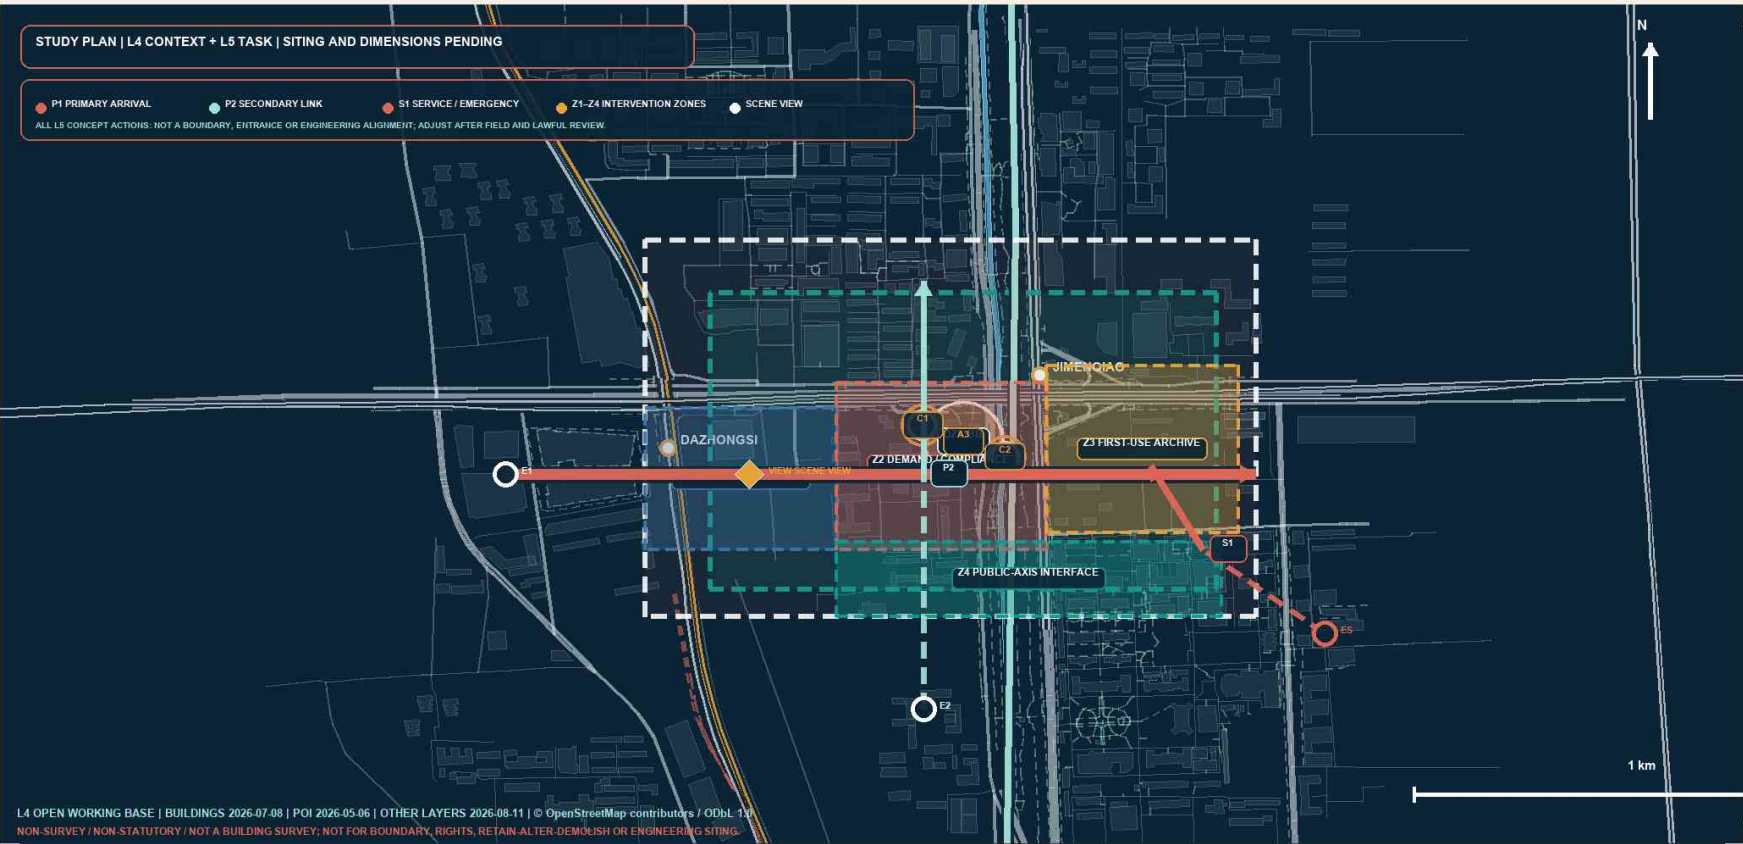

MAPPED OBJECTS AND REVIEW INTERFACES

WINDOW	KEY-003
AUDIT	AN-003
SECTION	SEC-DZS-AA / SEC-DZS-BB
COMPONENT	DC-DZS-001 / DC-DZS-002
PLAN ACTIONS	E1/E2/ES + P1/P2/S1 + Z1-Z4 + VIEW

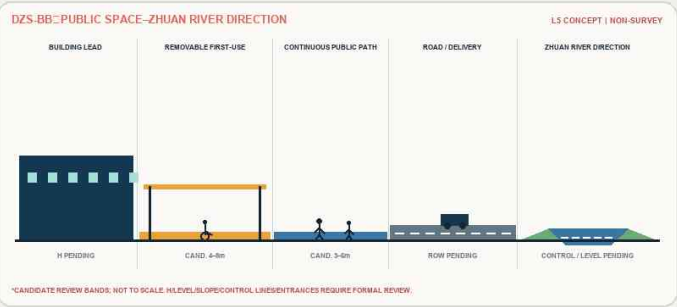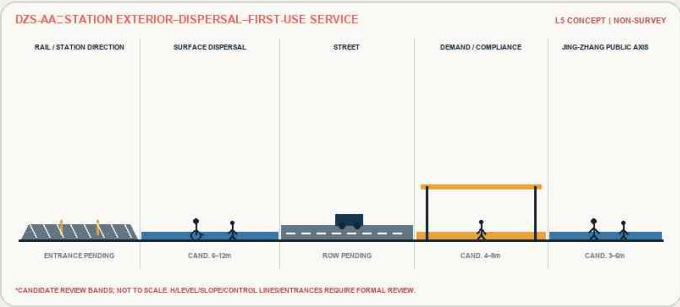

SPACE-OPERATION-EXIT LOOP




G0-G6 retains an audit trail; keep BLOCK if any site, rights, public, risk, cost, procurement or exit condition remains open.

S01 / SIX CUT-LINES AND VARIABLE INTERFACES

Three Key Areas: Plan Location and Site-Concept Sections for Six Cut-Lines

AA/BB alignments are L5 study indexes; candidate width reviews, human scale and interface relationships do not establish surveyed conditions, statutory control lines, building heights, levels, entrances or engineering dimensions.

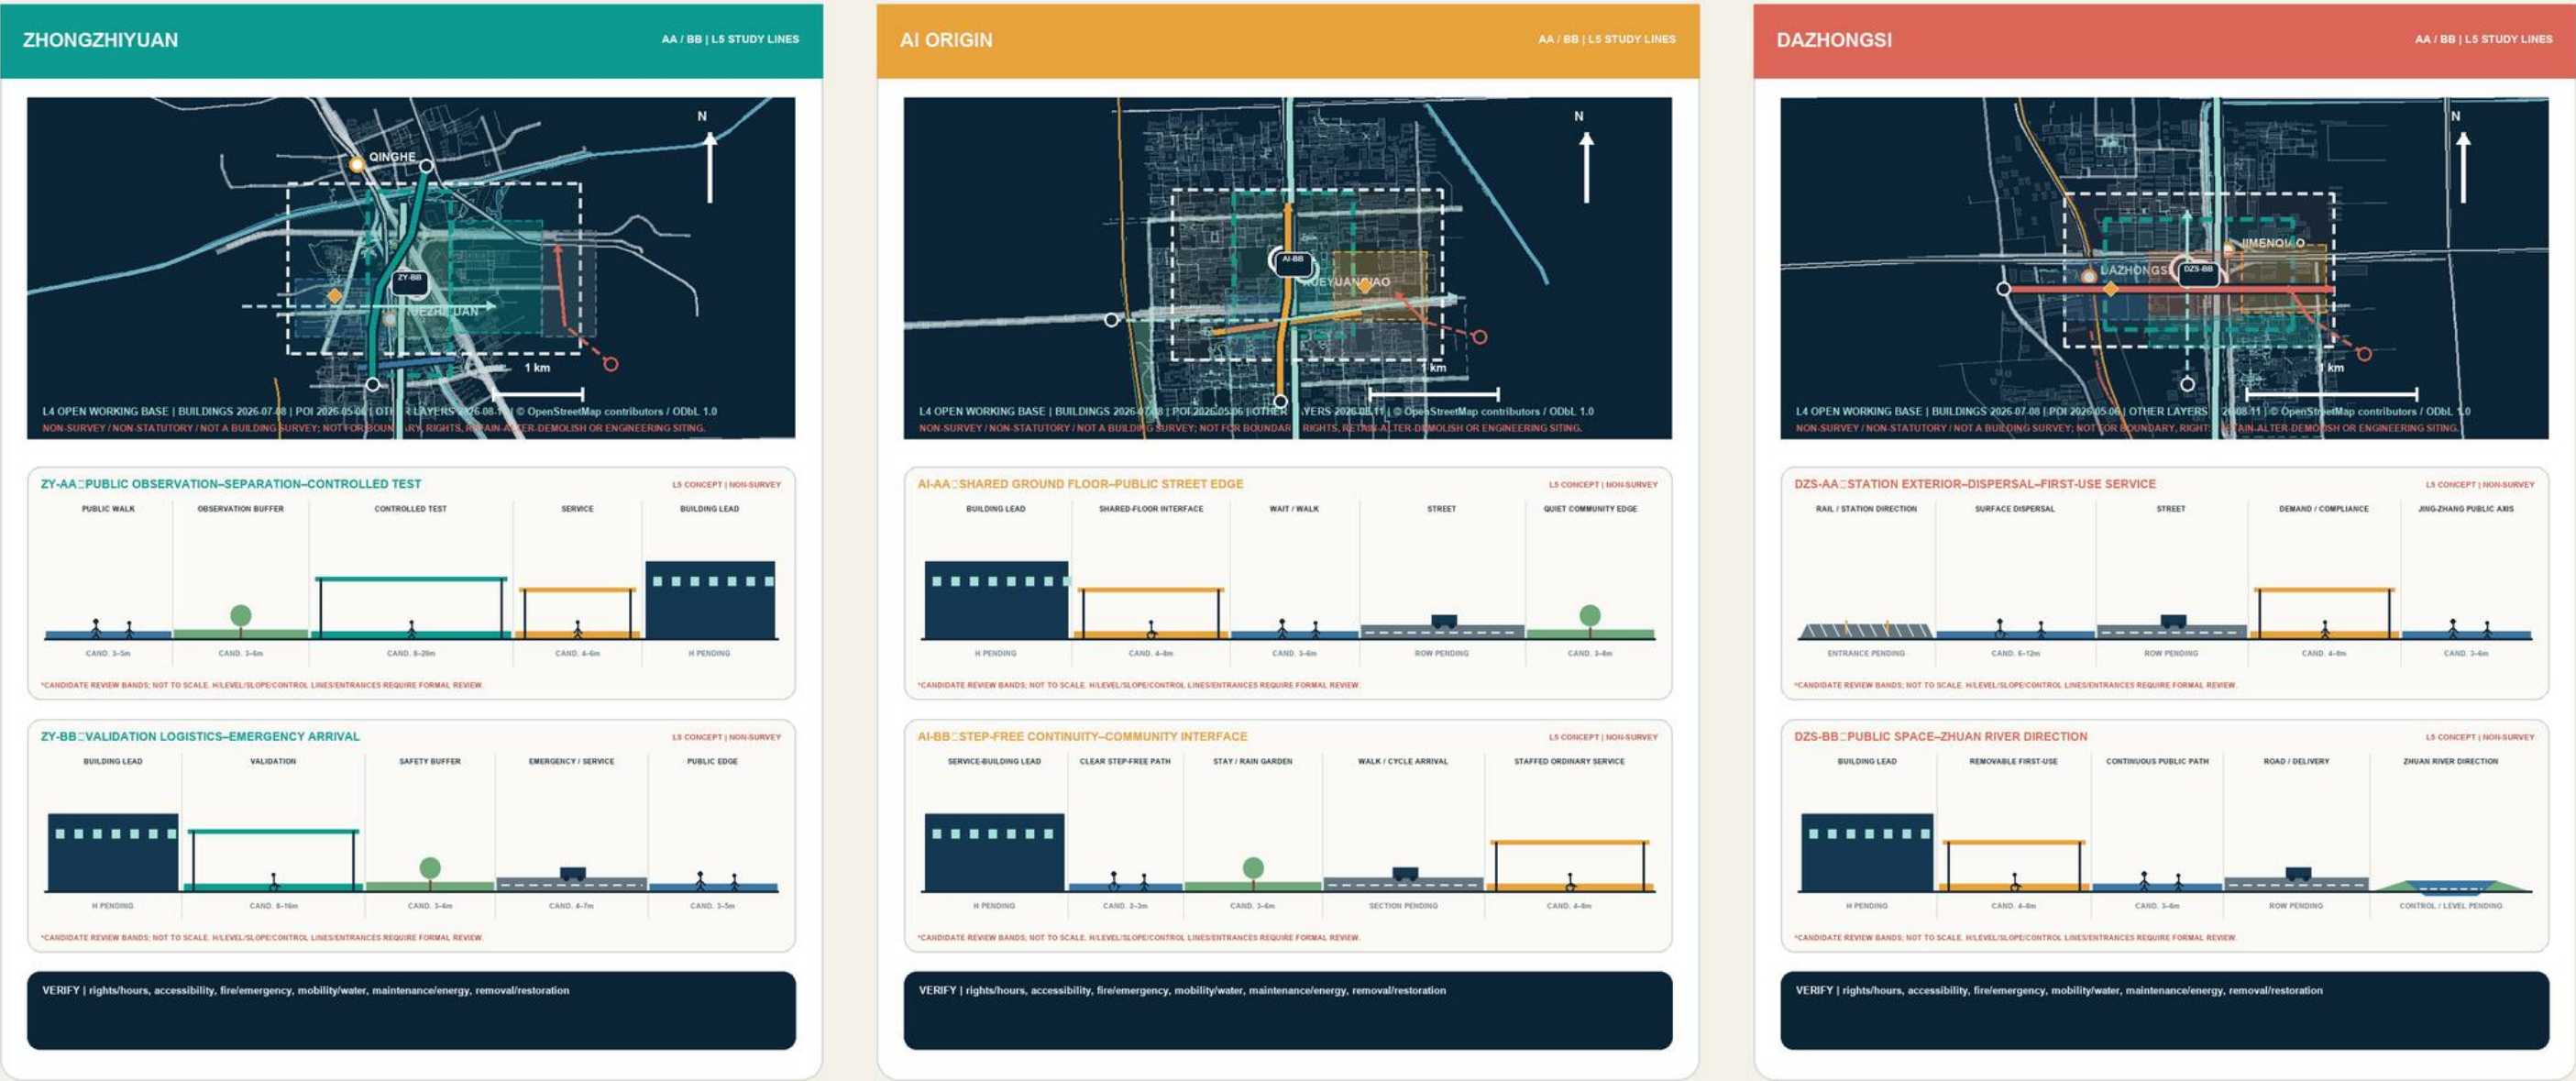

E01 / FOUR VERIFIABLE LOOPS

Spatial–AI–Delivery–Public Value: Four Verifiable Loops

All values count package, contract and verification-task completeness; they are not field performance, statutory metrics, approval or secured funding.

01 SPATIAL EVIDENCE

1 + 3 + 3	axis / corridors / study windows
9 + 8	field-audit segments / anchors
6 + 6	variable sections / reversible components

L5 provisional geometry; official boundary, rights and baseline remain pending.

02 AI GOVERNANCE

12 / 12	dual independent-gate coverage
12 / 12	human final-review coverage
72 / 1,498	synthetic branches / passed assertions

All 60 defect branches fail closed; synthetic PASS does not prove real-world efficacy.

03 DELIVERY HANDOFF

3	whole-life project registers
G0–G6	seven gates: evidence to exit
8 + 10	handoff checks / cost-evidence items

Role placeholder–lawful appointment–written receipt; unverified prices stay outside totals.

04 PUBLIC VALUE

12 / 12	ordinary-service equivalence
12 / 12	exit-restoration receipt coverage
90 / 180	post-deployment review points



Refusing AI adds no charge, unreasonable wait or off-site trip; appeals go to people.

SPATIAL SCALE (READ BY EVIDENCE LEVEL): official written study scale ≈11.4 km² | three key-area task scales total ≈368.4 ha | L4/L5 boundary diagnostic ≈413 m.
PENDING: official boundaries | FAR and height | building baseline and rights | continuously open length | quantities, prices, budget and accountable entities.

D00 / EVIDENCE & BOUNDARY

Evidence, Boundary and Design-Depth Control

Review confirmed facts, working basemap, provisional geometry and design proposals as separate evidence classes.

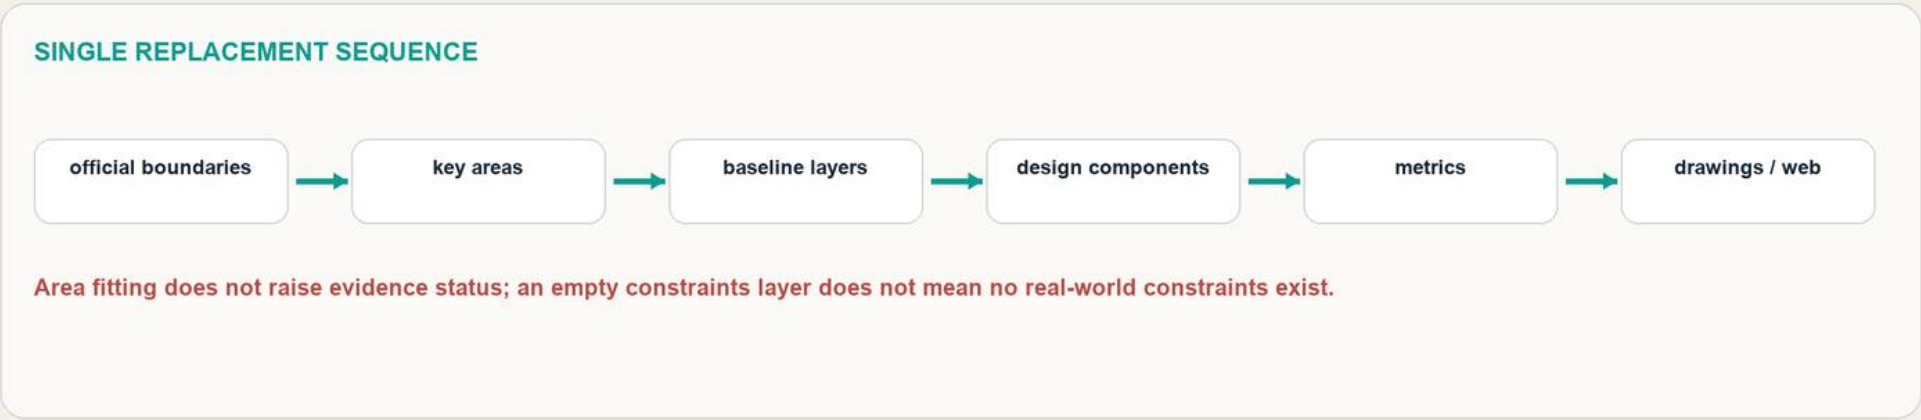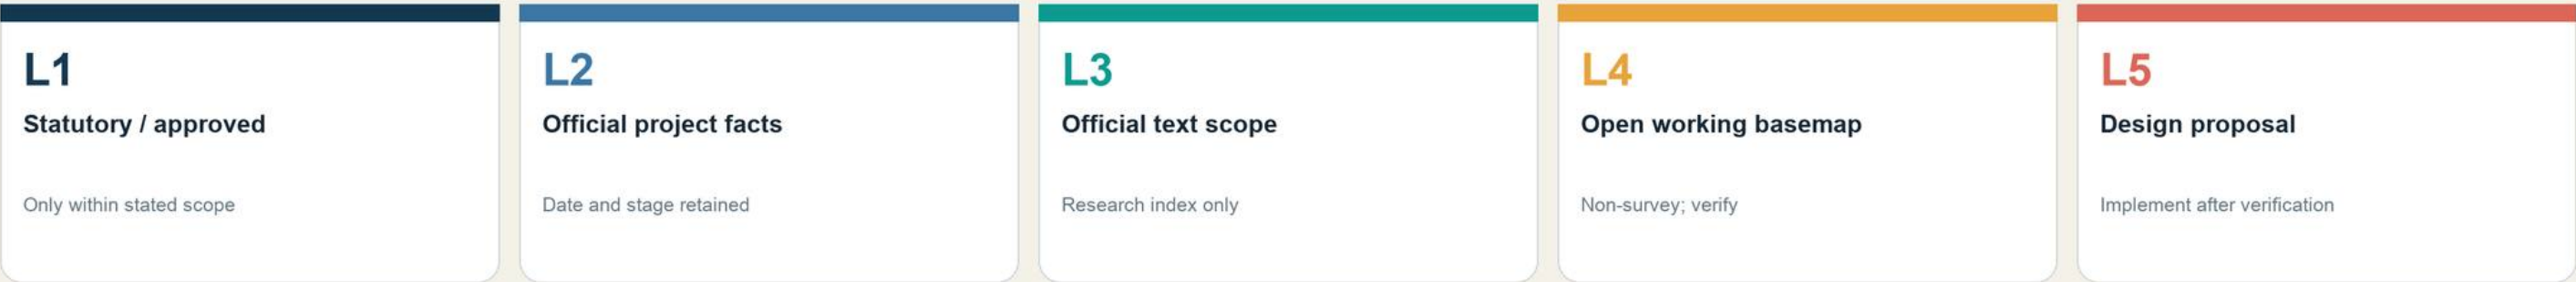

P0 DATA GAPS


- Official vector boundaries
- Parcels and rights
- Building survey / structure / fire
- Road lines and traffic counts
- Rail protection conditions
- River and flood controls
- Heritage coordinates
- Utility capacity
- Budget, procurement and 5-year OPEX

AI01 / SERVICE BLUEPRINTS

Three AI Concept Prototype Specifications


Each prototype delivers a service blueprint, spatial interface, data flow, responsibility matrix, and acceptance/stop criteria.

S01 Trusted model / edge-device test

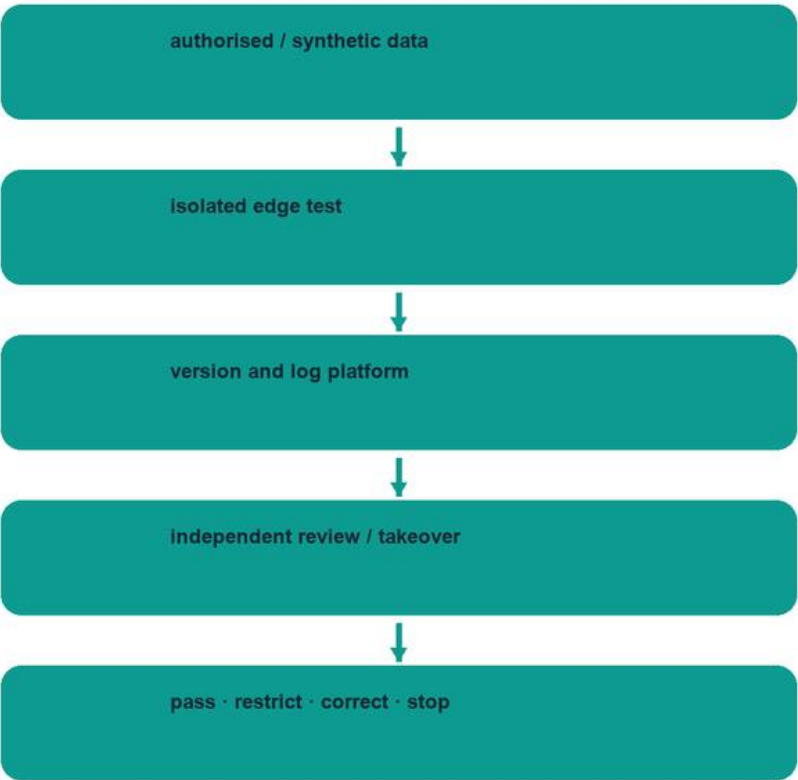


STOP: unclear provenance / no human fallback / severe incident unresolved / rights risk exceeds benefit

S06 Inclusive public-service assistant

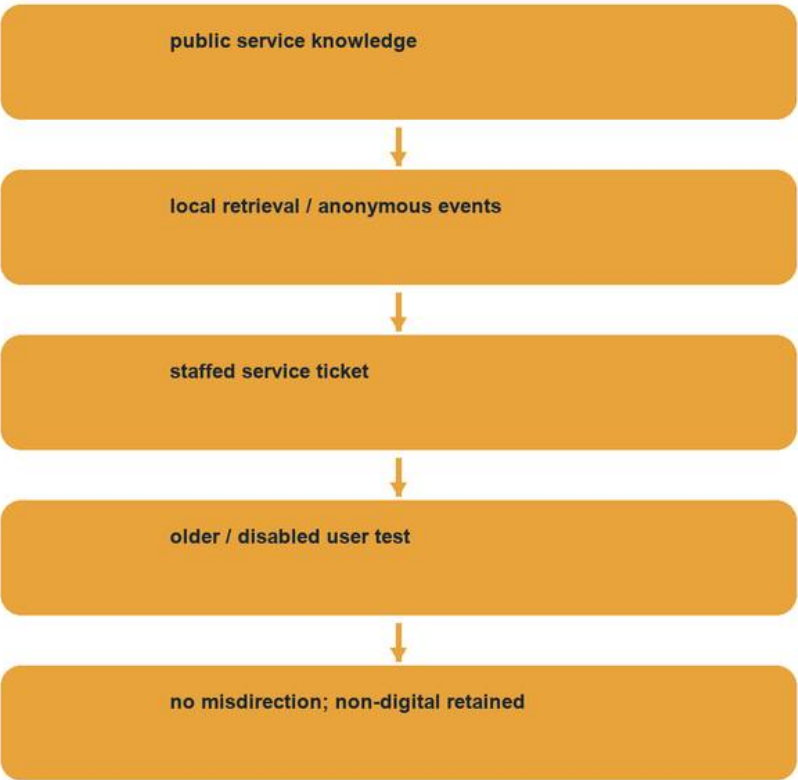

STOP: unclear provenance / no human fallback / severe incident unresolved / rights risk exceeds benefit


S11 First-use conversion and review

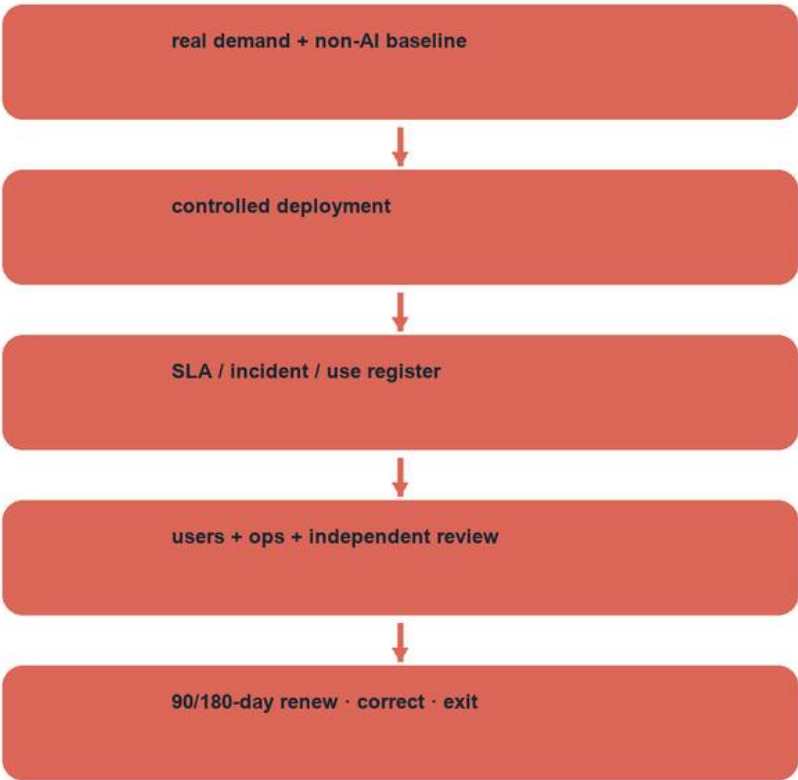

STOP: unclear provenance / no human fallback / severe incident unresolved / rights risk exceeds benefit

Public Participation, Public Value and Risk-Governance Loop

Public participation is embedded in demand formation, prototype observation, operating review and exit decisions.

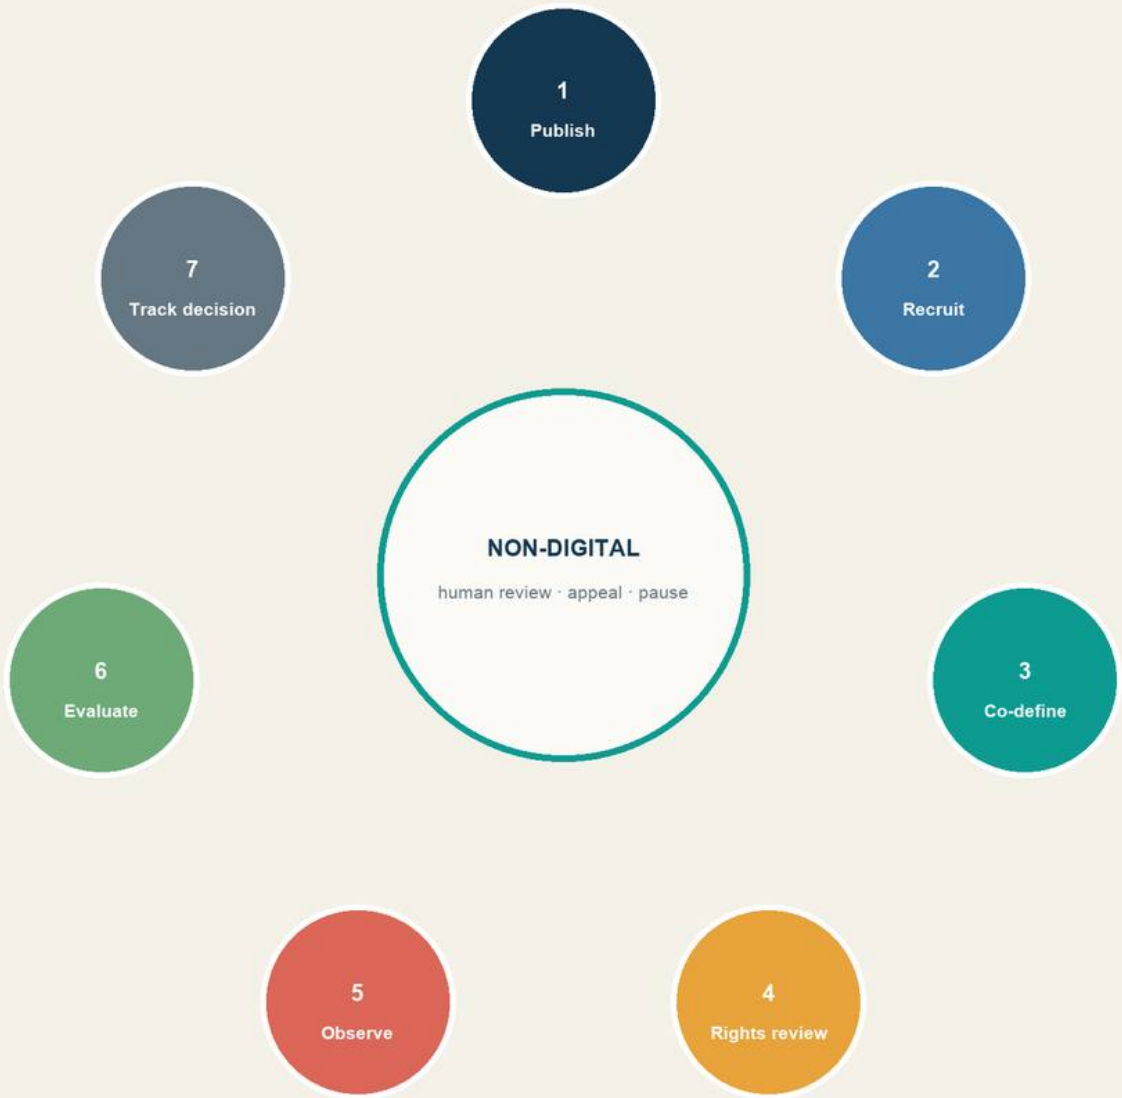

PROPOSED STARTING CONTROLS

Demand-brief completeness	≥95%
Public response rate	≥90%
High-risk takeover coverage	100%
Severe safety/privacy events	0
Critical accessibility barriers closed	100%
Exit completion	100%

MANDATORY PAUSE / EXIT TRIGGERS

- Demand owner or site rights unclear
- Unclear data provenance, version or legal basis
- No human fallback in a high-risk scenario
- Severe safety, privacy or fairness issue unresolved
- Whole-life cost or operations unaffordable
- No exit provision, deletion or alternative service

Targets enter formal performance documents only after baseline survey, professional review and confirmation by the lawfully determined responsible entities; they are not government commitments.

B01 / IDENTITY & LANDMARK KIT

RailWeave Identity System and Three Reversible Landmarks

Identity is built around project status, evidence and public service—not corporate logos, giant screens or permanent monuments.

RAILWEAVE



FIVE EVIDENCE COLOURS

L1

L2

L3


L4

L5

Tactile code | easy-read type | low-reflectance material | replaceable parts | low-glare night lighting

01

Validation Results Gallery

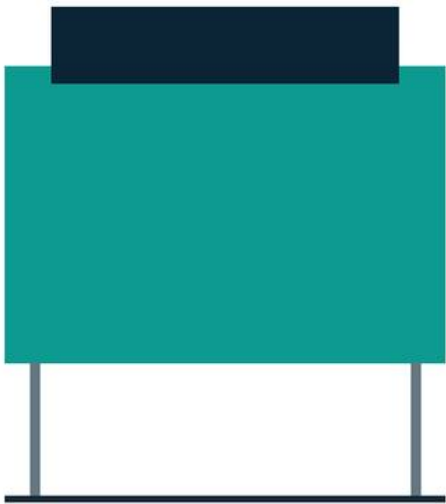


- pass/restrict/correct/stop
- model version + human review
- redacted summary

site, fire, maintenance and restoration to verify

02

Collaborative Innovation Courtyard

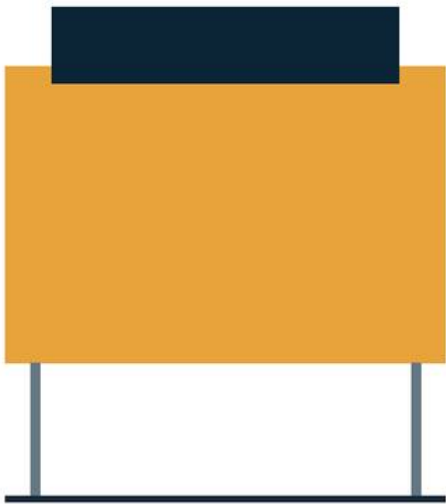


- paper/digital demand wall
- objection and exit record
- movable accessible parts

site, fire, maintenance and restoration to verify

03

First-Use Conversion Gateway

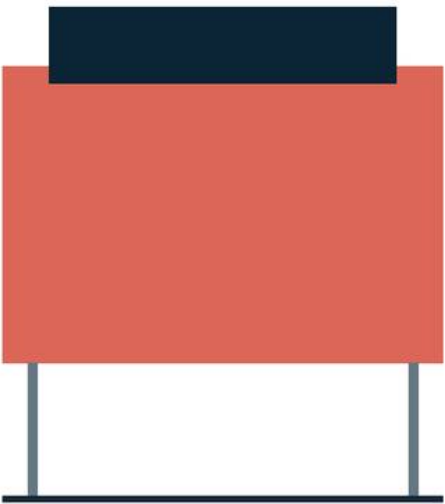

- demand-validation-procurement
- 90/180-day review
- rail mileage / project ID

site, fire, maintenance and restoration to verify

RECALCULATE AS ONE PACKAGE WHEN OFFICIAL INPUTS ARRIVE

- official boundaries and regulatory drawings
- parcels, rights and building survey
- road, metro, railway, water and heritage controls
- utility capacity, procurement budget and five-year operating account
- field accessibility and opening-status survey

RECALCULATION PACKAGE

- boundary–geometry–metrics–drawings
- one version, date and responsibility chain
- retain superseded values; no silent overwrite

FIELD AND PROFESSIONAL REVIEW

- opening, accessibility, crossings and night use
- mobility, utilities, water, fire and heritage
- data security, procurement, insurance and audit

GATE AND EXIT RECORD

- entities, rights and written responsibility
- five-year total cost and funding sources
- acceptance, correction, pause and restoration receipt

This package is not a statutory plan, engineering design, investment decision, procurement result or approval basis.
